

Short Term Overview

Deanbank House & Canaan Lane



W/C 03/08/20

1 – Backfill cable joint excavation and remove fences.

2 – Install walkway tower over footpath.

3 – Commence groundworks for foundations.

4 – Complete drainage installation, surfacing, and fences.

5 – Pour concrete slab for ASHP.

6 – Prepare and pour retaining wall foundation.

7 – Footpath alteration to Canaan Lane.

8 – Temporary access road remains.

W/C 10/08/20




1 – Progress groundworks.

2 – Continue retaining wall foundation.

3 – Temporary access road remains.

4 – Playground area available for Deanbank House.

W/C 17/08/20

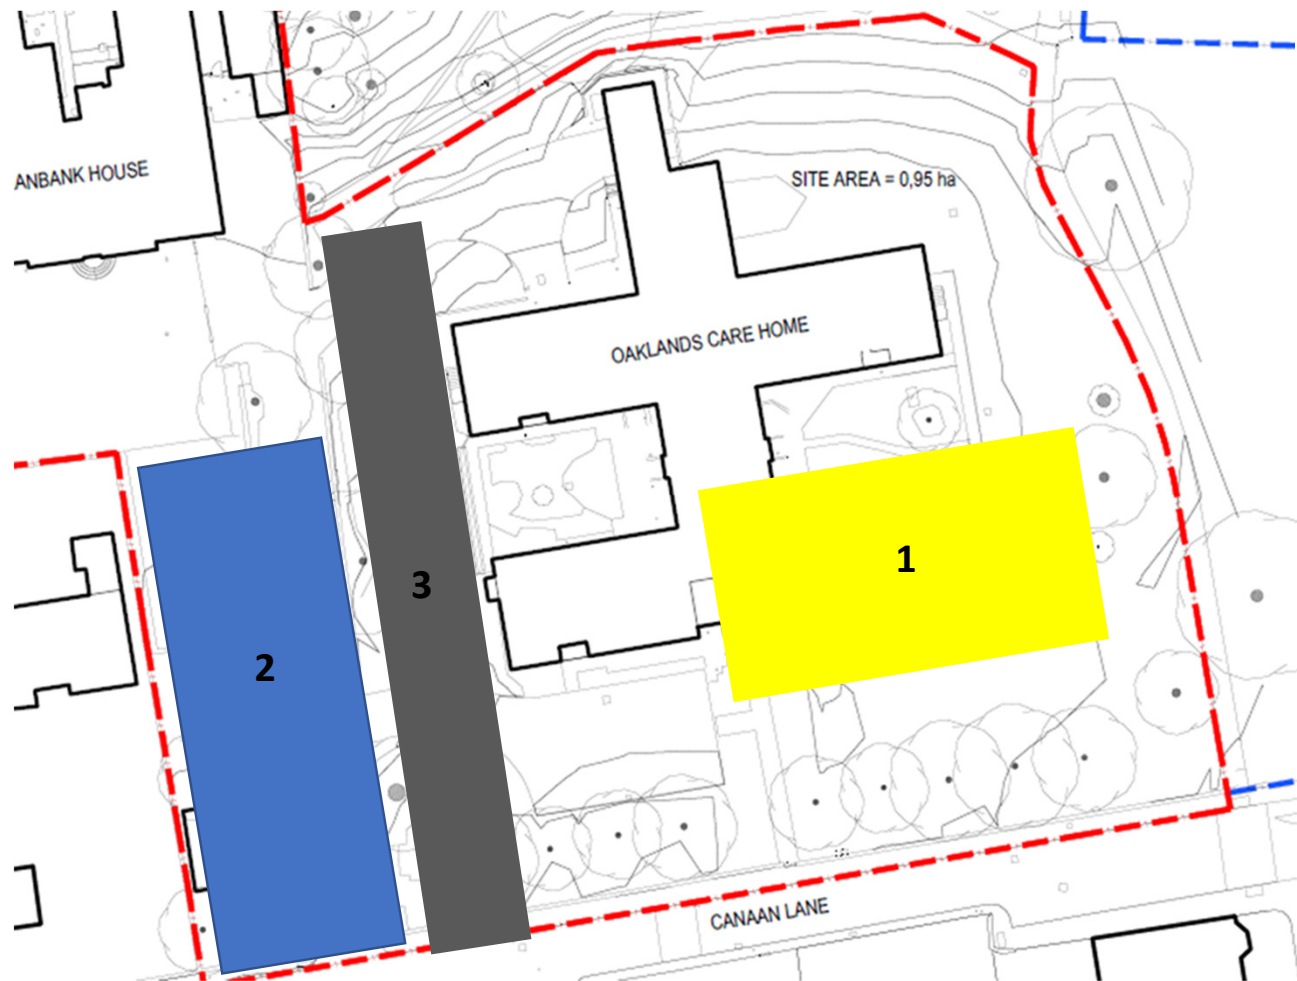


1 – Progress groundwork and foundations.

2 – Progress drainage installation.

3 – Temporary access road remains.

W/C 24/08/20

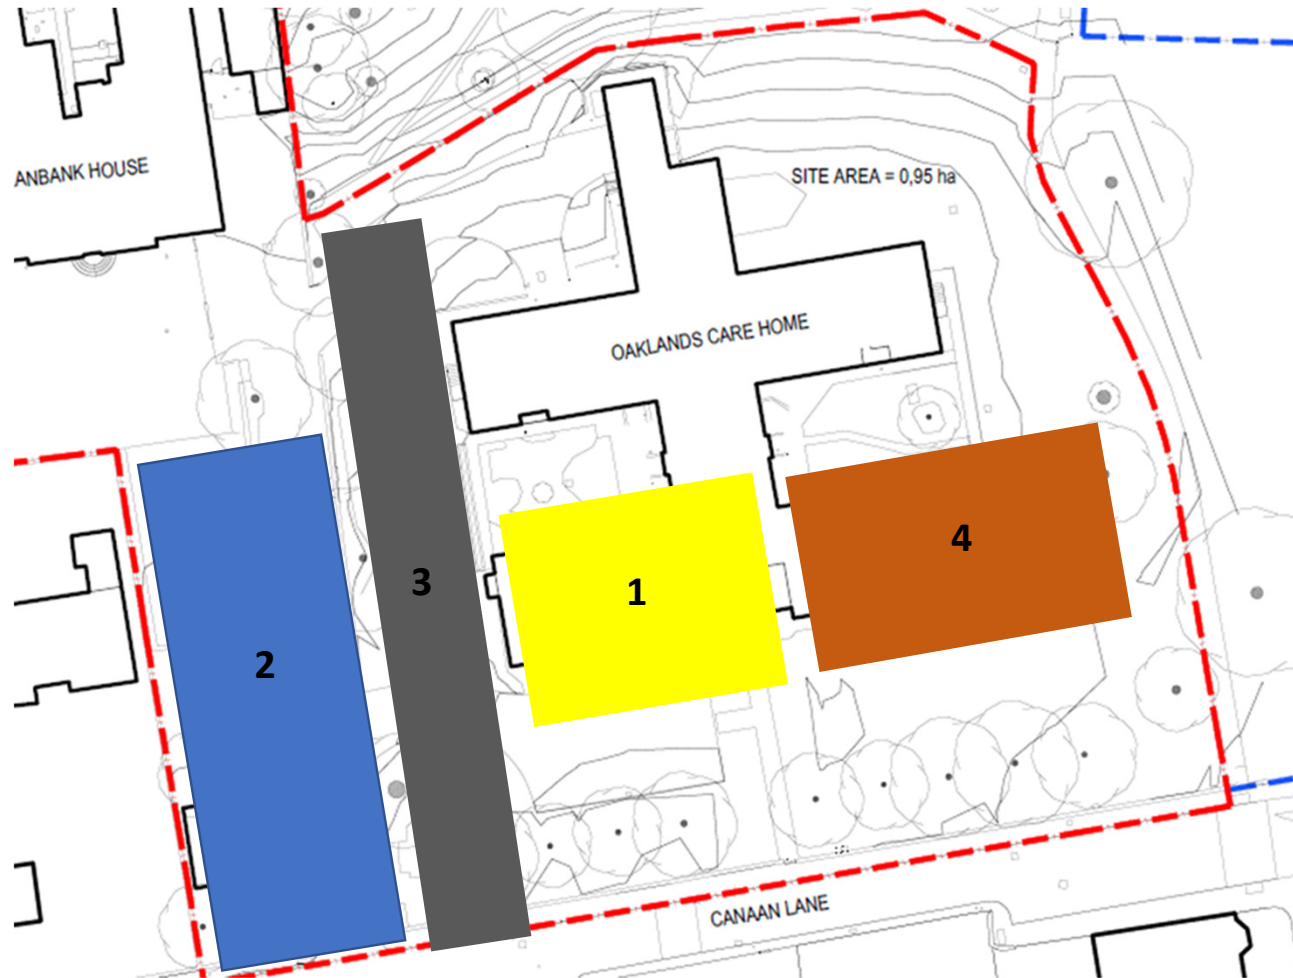

1 – Progress groundwork and foundations.

2 – Progress drainage installation and grading.

3 – Temporary access road remains.


4 – Commence steel frame.

W/C 31/08/20



- 1 – Complete phase 1 groundwork and foundations.
- 2 – Grading to prepare for surfacing.
- 3 – Temporary access road remains.
- 4 – Progress steel frame.
- 5 – Install boundary hoarding fences (temporary)

W/C 07/09/20

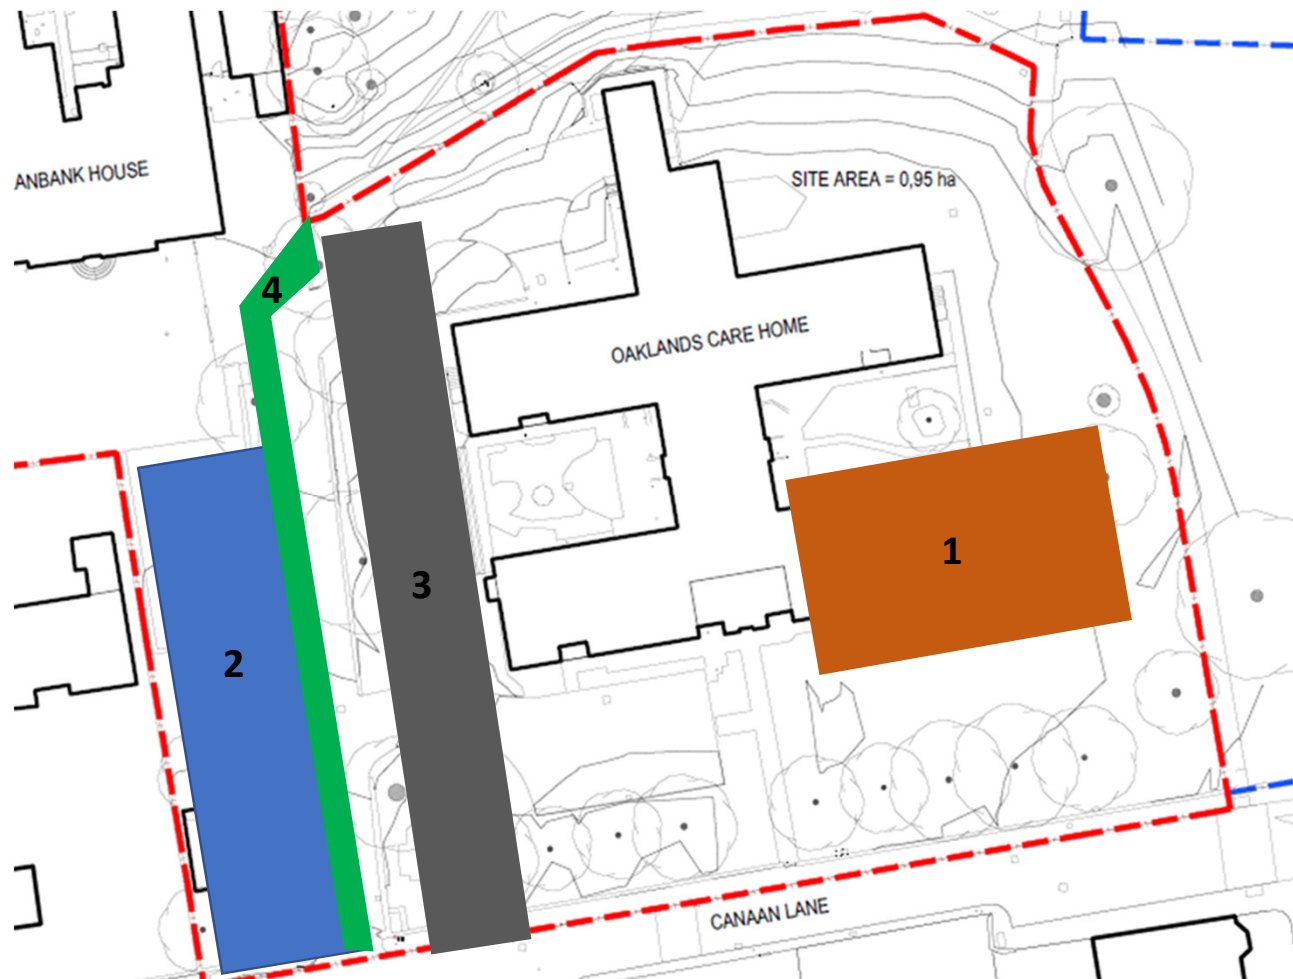


1 – Progress steel frame.

2 – Surfacing.

3 – Temporary access road remains.

4 – Install boundary hoarding fences (temporary)

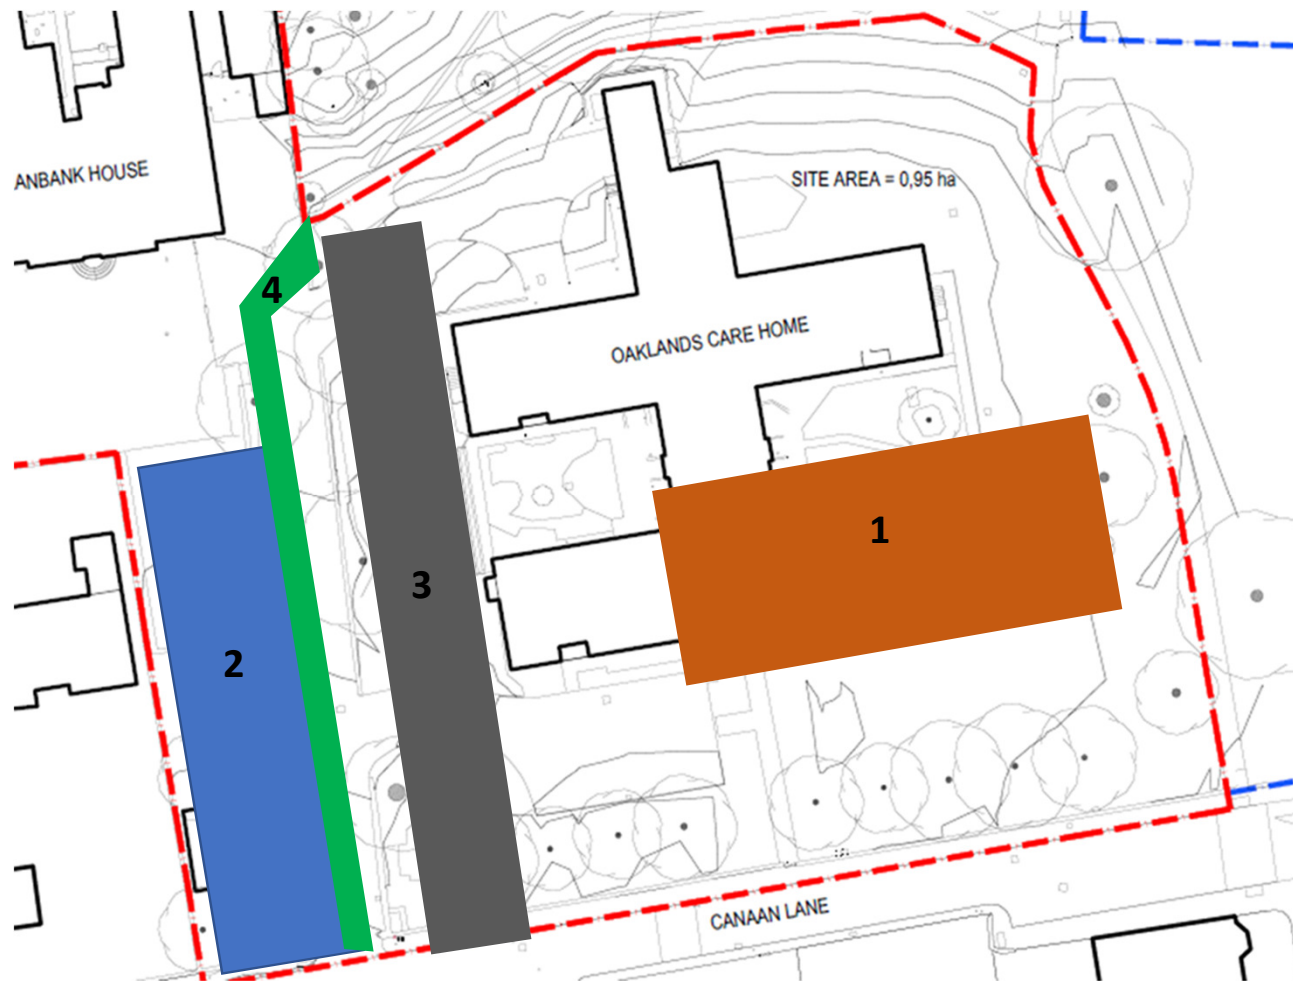

W/C 14/09/20

1 – Progress steel frame.

2 – Install gates.

3 – Temporary access road remains.

4 – Complete boundary hoarding fences (temporary)

W/C 21/09/20



1 – Progress metal deck (1st floor slab)

2 – Demolish stone wall and remove temporary road.

3 – Area available for Deanbank House.

W/C 28/09/20



1 – Progress 1st floor slab

2 – Commence groundworks and foundations.
